



TSP-NEW BUILD



Layout:TSP

2014

Activity ID	Activity Name	Original Duration	Start	Finish	Physical % Complete	Total Float	2014																			
							June 08	15	22	29	July 06	13	20	27	August 03	10	17	24	31	September 07	14	21	28	October 05	12	19
TSP-NEW BUILD							TSP-NEW BUILD																			
PRE CONSTRUCTION							PRE CONSTRUCTION																			
A1000	Receive Porta Potty	0d	Jun-16-14*		0%	36d	Receive Porta Potty, Milestone																			
A1020	Demolition	2d	Jun-16-14	Jun-17-14	0%	36d	Demolition																			
CONSTRUCTION							CONSTRUCTION																			
CIVIL							CIVIL																			
Grounds							Grounds																			
A1030	Grading/Excavation	19d	Jun-18-14	Jul-07-14	0%	36d	Grading/Excavation																			
Foundations							Foundations																			
A1040	Pour Foundation Footers	19d	Jun-18-14	Jul-07-14	0%	36d	Pour Foundation Footers																			
A1050	Termite Pre-Treat	19d	Jun-18-14	Jul-07-14	0%	36d	Termite Pre-Treat																			
A1060	Pour Basement Walls	19d	Jun-18-14	Jul-07-14	0%	36d	Pour Basement Walls																			
A1070	Pour Deck/Porch	19d	Jun-18-14	Jul-07-14	0%	36d	Pour Deck/Porch																			
A1080	Waterproofing	19d	Jun-18-14	Jul-07-14	0%	36d	Waterproofing																			
A1090	Backfill	19d	Jun-18-14	Jul-07-14	0%	36d	Backfill																			
A1360	Driveway	21d	Sep-11-14	Oct-01-14	0%	36d	Driveway																			
A1370	Walkways	21d	Sep-11-14	Oct-01-14	0%	36d	Walkways																			
STRUCTURAL							STRUCTURAL																			
Framing							Framing																			
A1100	Basement	21d	Jul-08-14	Jul-28-14	0%	36d	Basement																			
A1110	First Floor	21d	Jul-08-14	Jul-28-14	0%	36d	First Floor																			
A1120	Second Floor	21d	Jul-08-14	Jul-28-14	0%	36d	Second Floor																			
A1140	House Wrap	21d	Jul-08-14	Jul-28-14	0%	36d	House Wrap																			
A1150	Stairs/Interior	21d	Jul-08-14	Jul-28-14	0%	36d	Stairs/Interior																			
A1180	Frame Back Deck/Porch	21d	Jul-08-14	Jul-28-14	0%	36d	Frame Back Deck/Porch																			
Roofing							Roofing																			
A1130	Trusses	21d	Jul-08-14	Jul-28-14	0%	36d	Trusses																			
A1260	Roof Decking, Felt, and Shingles	8d	Aug-19-14	Aug-26-14	0%	36d	Roof Decking, Felt, and Shingles																			
A1480	Roof Leaders	14d	Oct-23-14	Nov-05-14	0%	36d	Roof Leaders																			
Exterior							Exterior																			
A1160	Install Windows and Window Wrap	21d	Jul-08-14	Jul-28-14	0%	36d	Install Windows and Window Wrap																			
A1170	Install Exterior Doors	21d	Jul-08-14	Jul-28-14	0%	36d	Install Exterior Doors																			
A1270	Exterior Trim	8d	Aug-19-14	Aug-26-14	0%	36d	Exterior Trim																			
A1280	Vinyl Siding	8d	Aug-19-14	Aug-26-14	0%	36d	Vinyl Siding																			
A1290	Stone Siding	8d	Aug-19-14	Aug-26-14	0%	36d	Stone Siding																			
A1300	Gutters	8d	Aug-19-14	Aug-26-14	0%	36d	Gutters																			
A1440	Exterior Painting	7d	Oct-16-14	Oct-22-14	0%	36d	Exterior Painting																			
Interior							Interior																			
A1320	Exterior Wall Insulation	7d	Aug-27-14	Sep-03-14	0%	36d	Exterior Wall Insulation																			
A1330	Attic Insulation	7d	Aug-27-14	Sep-03-14	0%	36d	Attic Insulation																			
A1340	Sheetrock Installation	7d	Sep-04-14	Sep-10-14	0%	36d	Sheetrock Installation																			
A1350	Sheetrock Finishing	7d	Sep-11-14	Sep-17-14	0%	36d	Sheetrock Finishing																			
A1420	Garage Door Opener	7d	Oct-02-14	Oct-08-14	0%	78d	Garage Door Opener																			
Interior Finishes							Interior Finishes																			
A1380	Hardwood Installation	15d	Sep-17-14	Oct-01-14	0%	36d	Hardwood Installation																			
A1390	Install Cabinets/Vanities	15d	Sep-17-14	Oct-01-14	0%	36d	Install Cabinets/Vanities																			
A1400	Interior Doors	15d	Sep-17-14	Oct-01-14	0%	36d	Interior Doors																			
A1410	Carpentry/Trim	15d	Sep-17-14	Oct-01-14	0%	36d	Carpentry/Trim																			

Actual Level of Effort
 Actual Work
 Critical Remaining Work
 Primary Baseline
 Remaining Work
 ◆ Milestone


Data Date:Jun-09-14



TSP-NEW BUILD



Layout:TSP

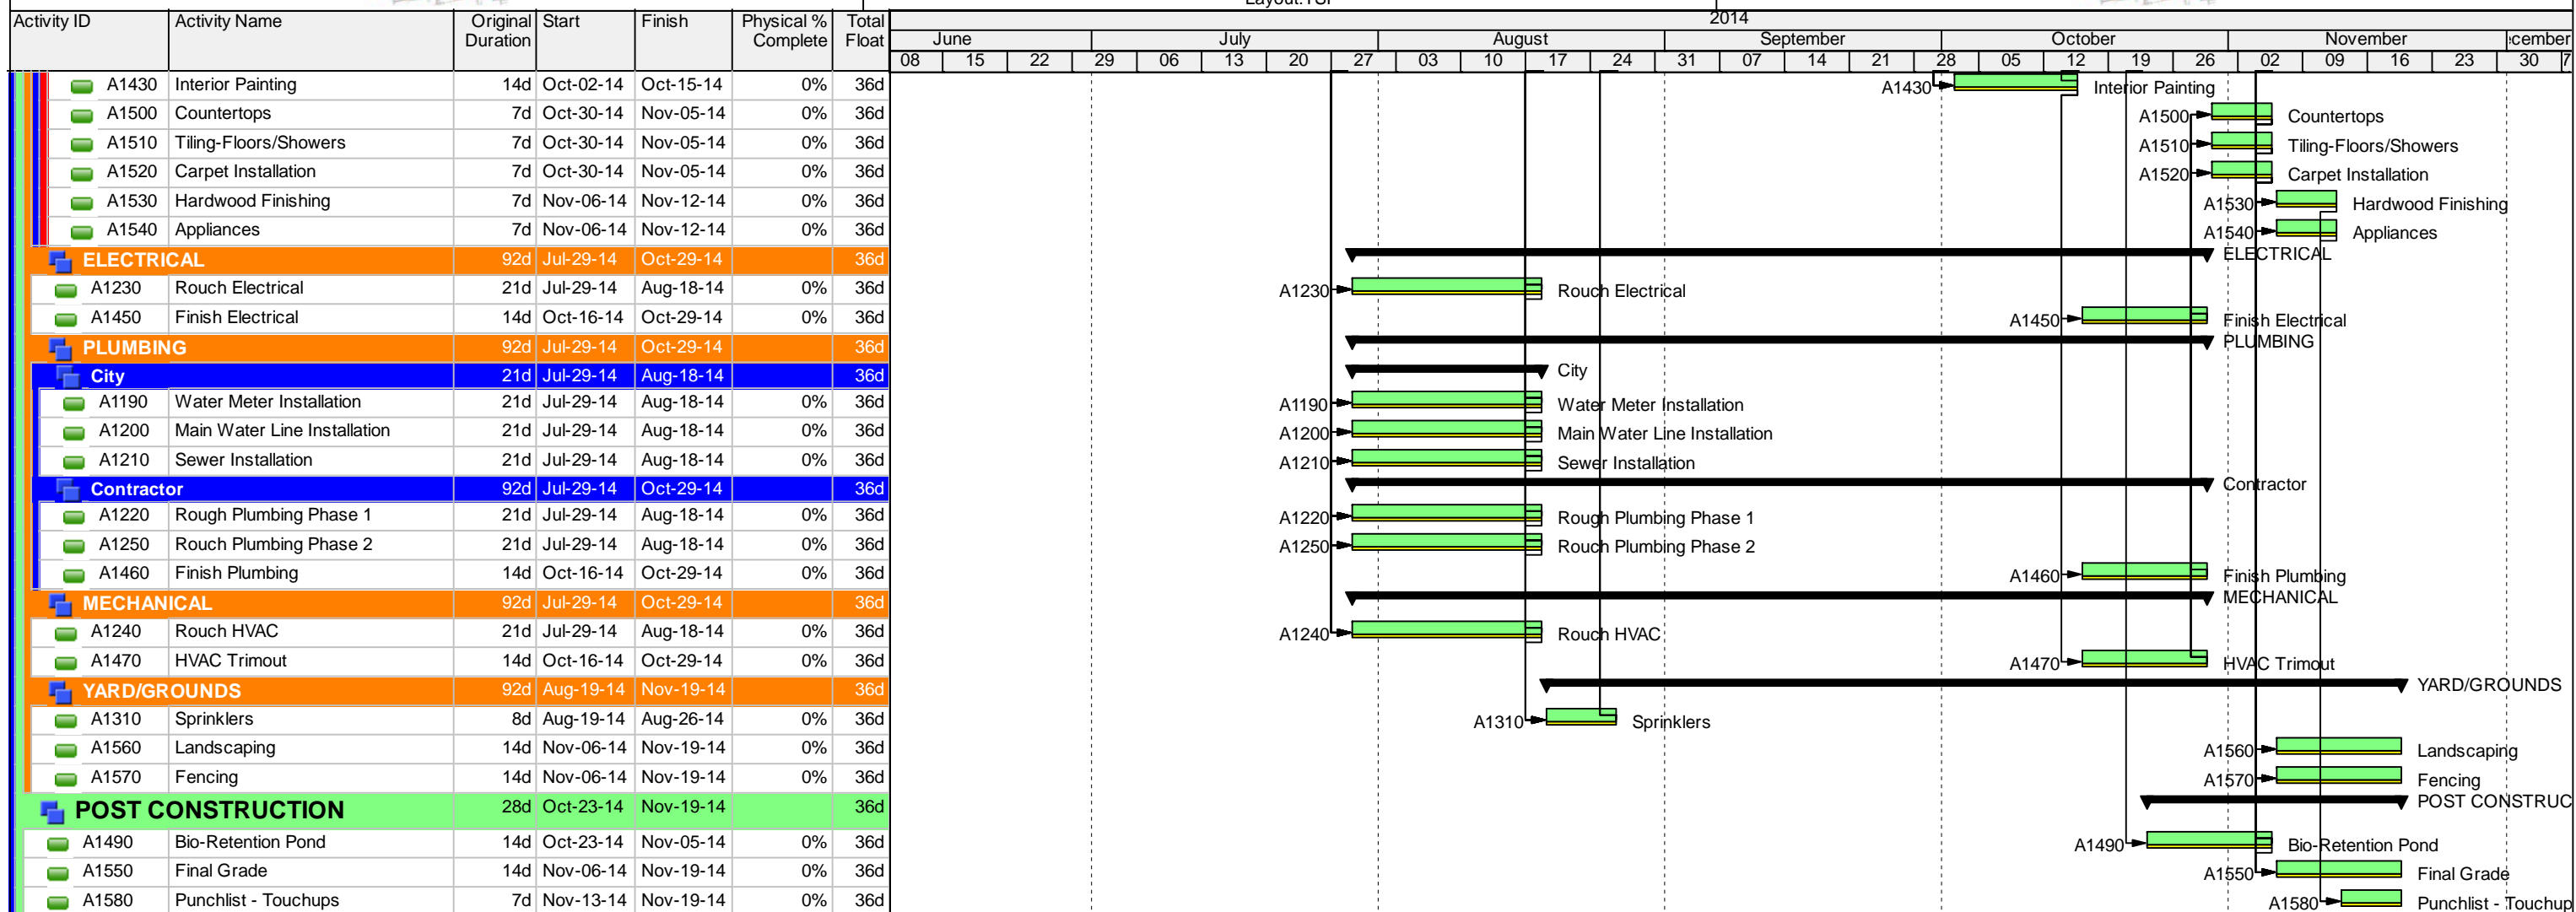

█ Actual Level of Effort
 █ Actual Work
 █ Critical Remaining Work
 Primary Baseline
 Remaining Work
 ◆ Milestone

Data Date:Jun-09-14
